# TISBURY SCHOOL

JOINT COMMITTEE MEETING MARCH 16, 2022









MEETING INFORMATION AVAILABLE ONLINE @

www.tisbury-school-project.com

# **A**GENDA

- Call to Order
- Attendance
- Tisbury School Construction Project Review Presentation
- Public Comment
- Adjournment

#### OWNER'S PROJECT MANAGER'S UPDATE

#### Milestone Schedule – "A Look Back"

Wrap-up Design Development Phase


Temporary School Modulars Procurement


Construction Manager at Risk Procurement


April 2021 – November 2021

December 2021 – February 2022


September 2021 – December 2021

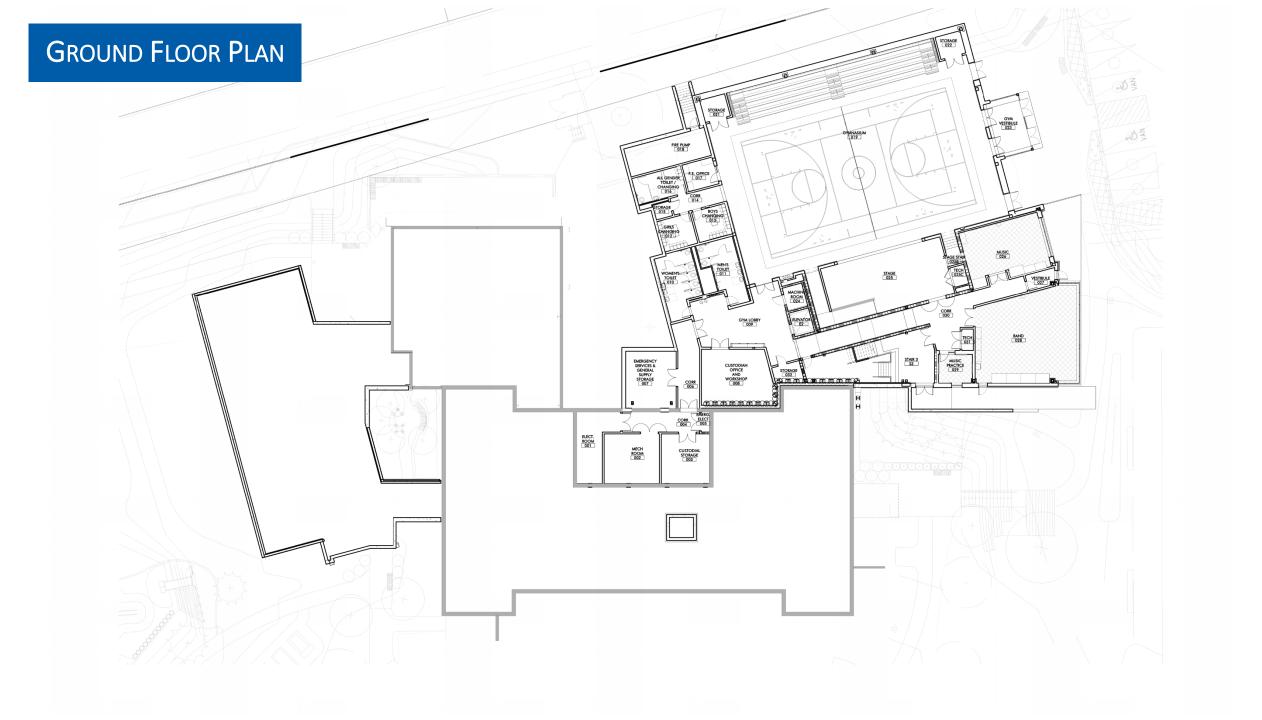

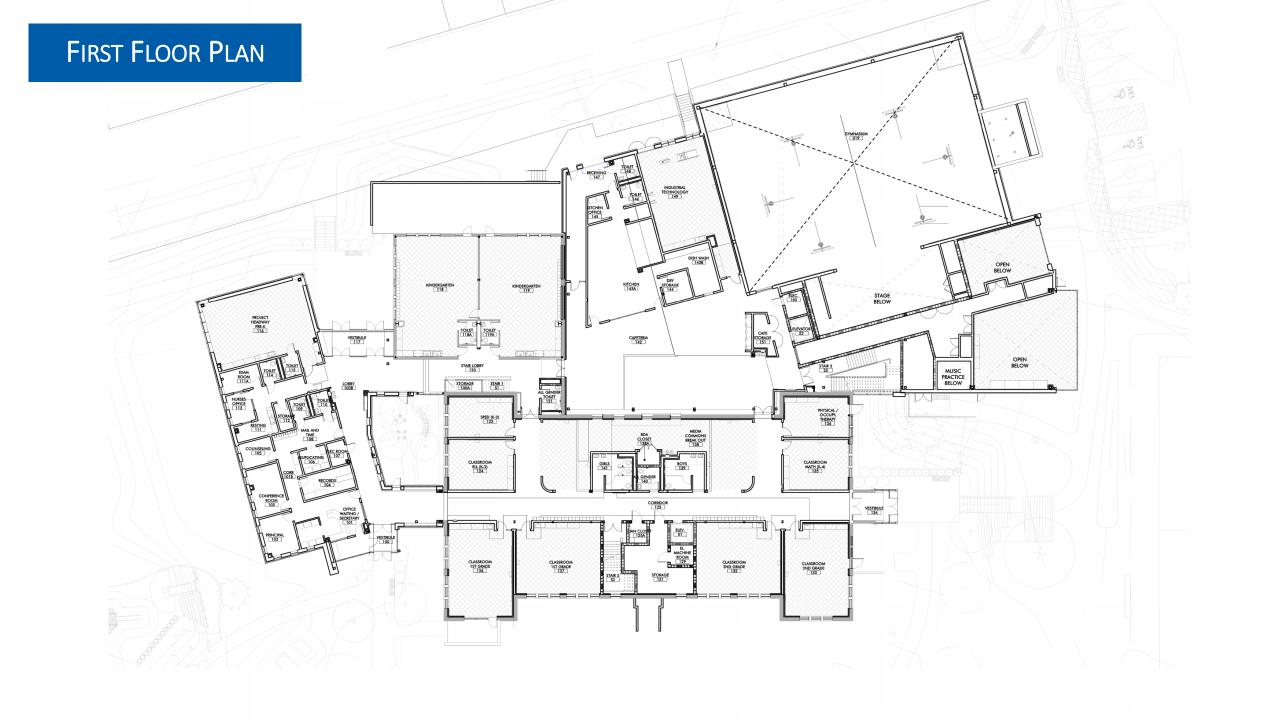

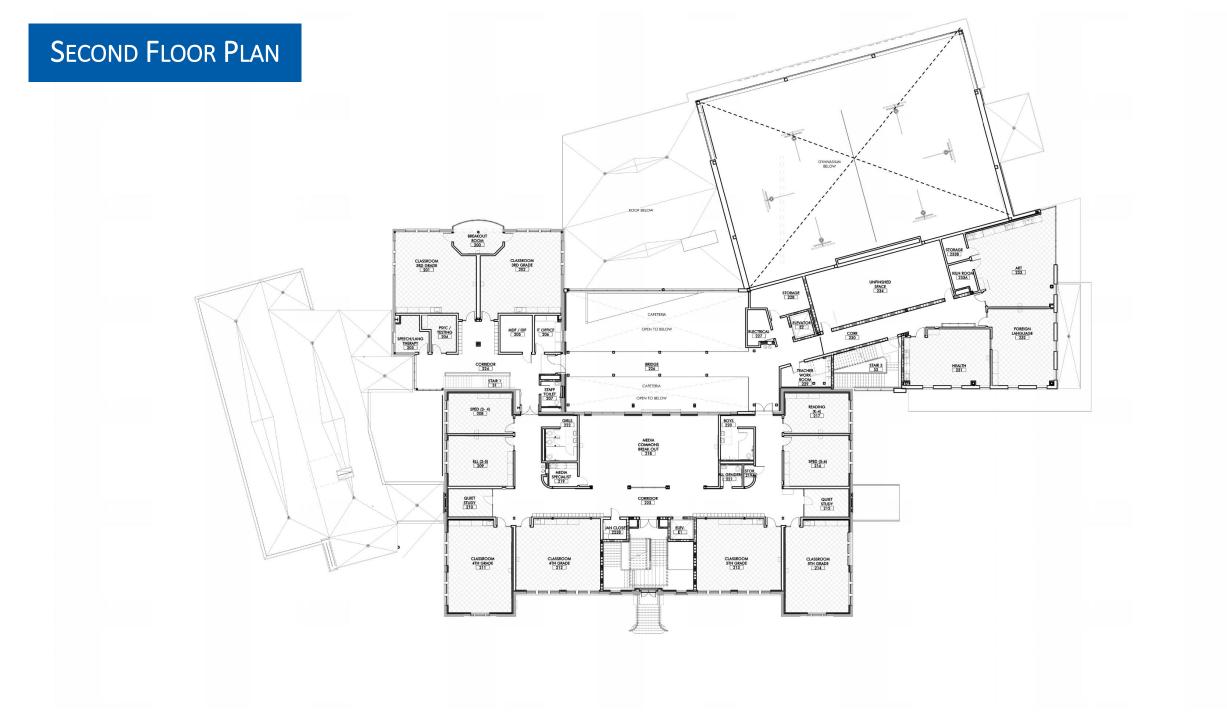

#### THIRD FLOOR PLAN

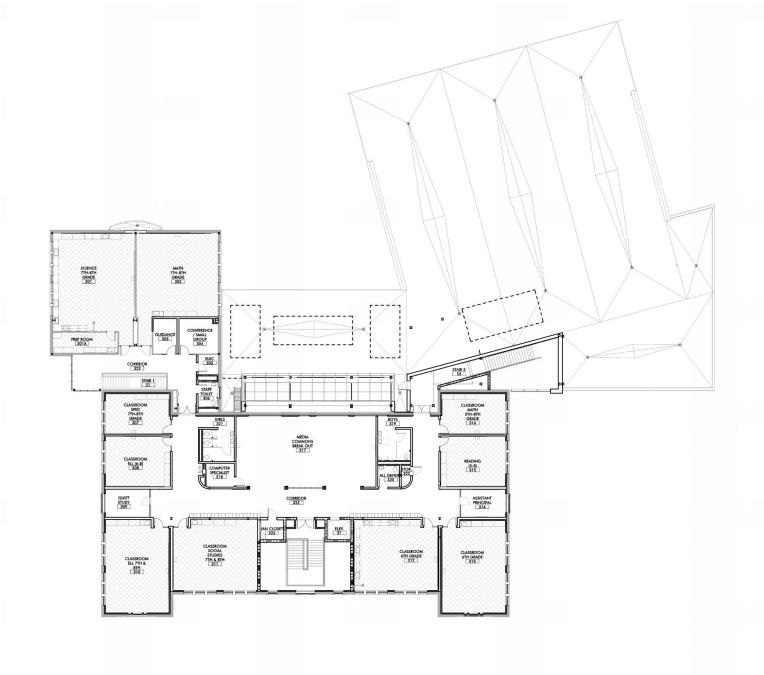


SITE LOGISTICS / PHASING












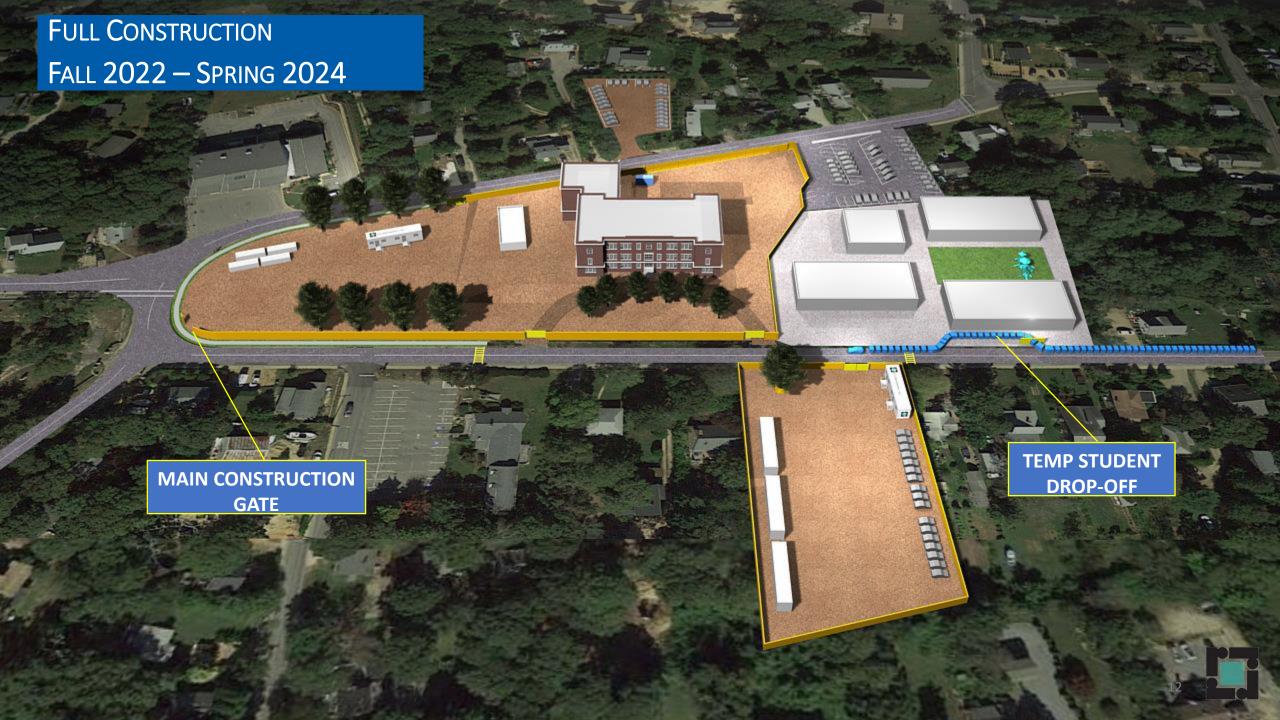


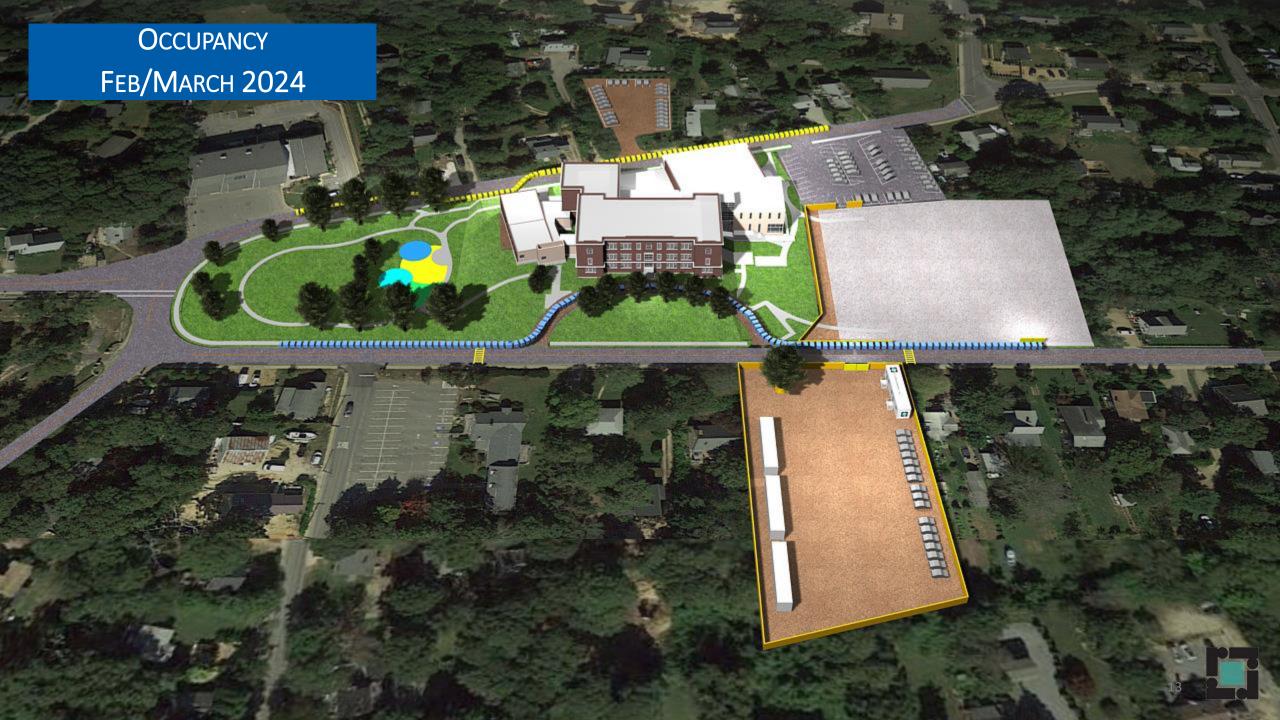

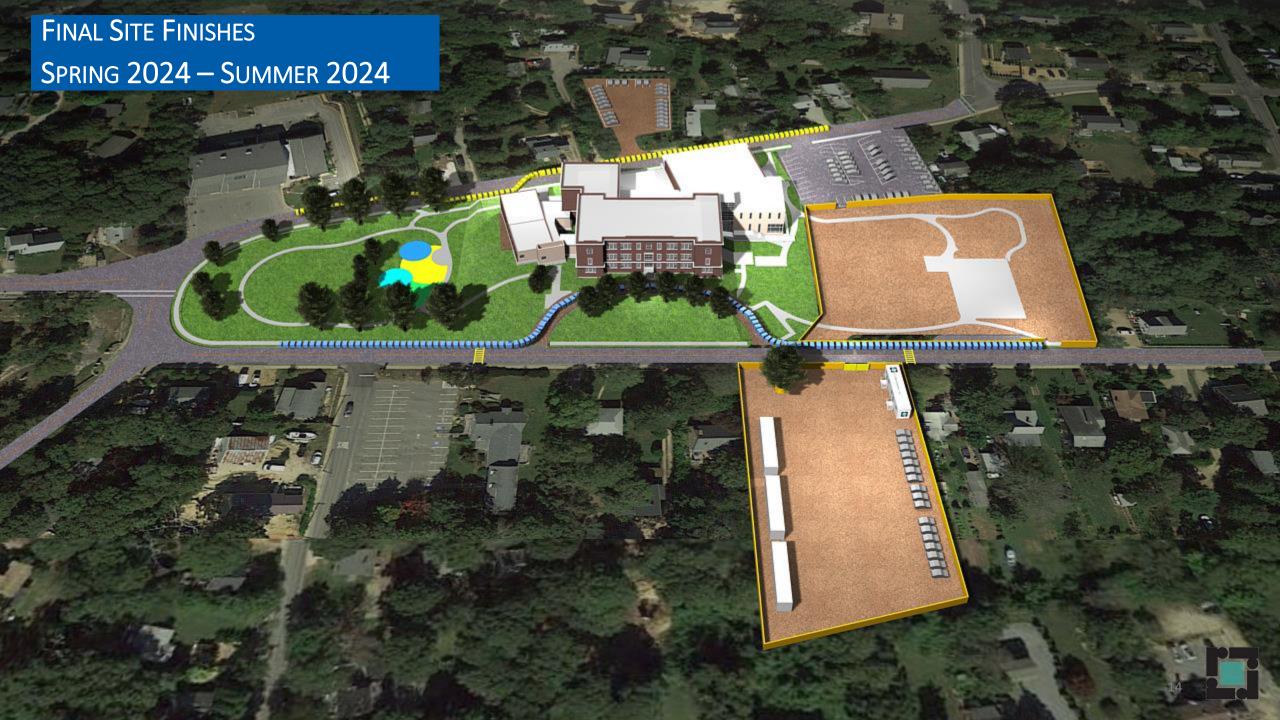

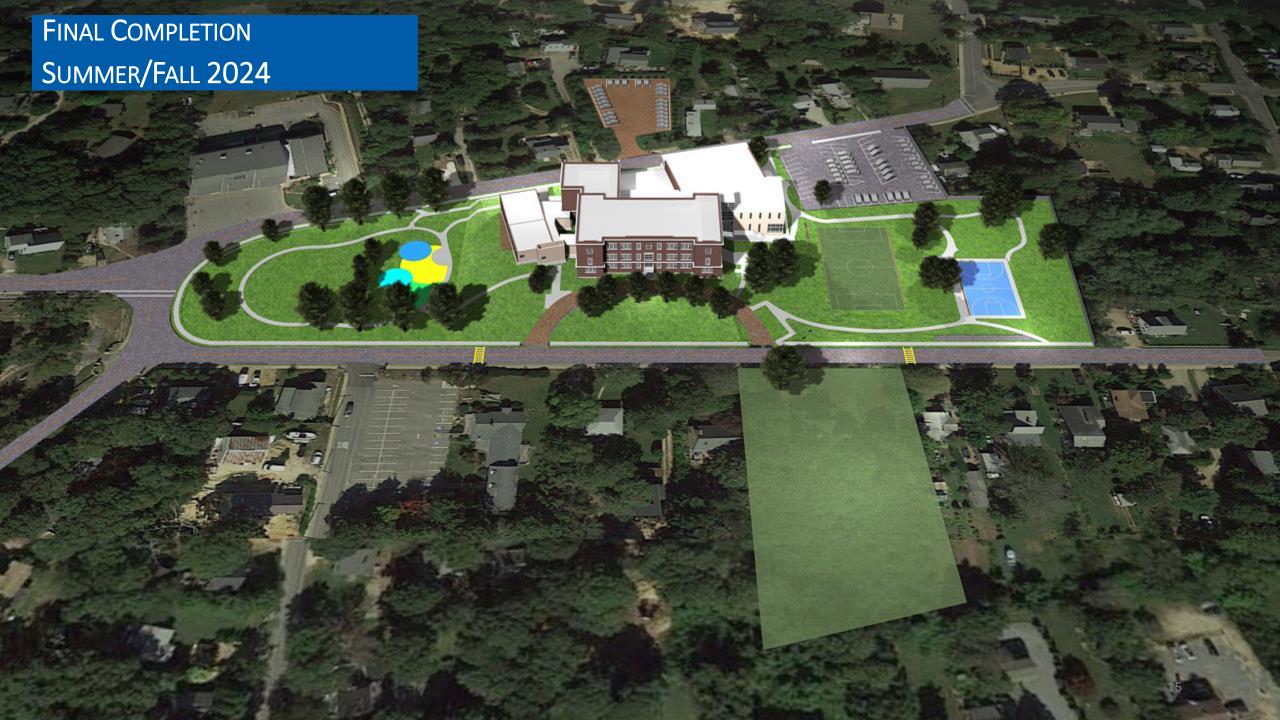

STUDENT DROP-OFF PLAN

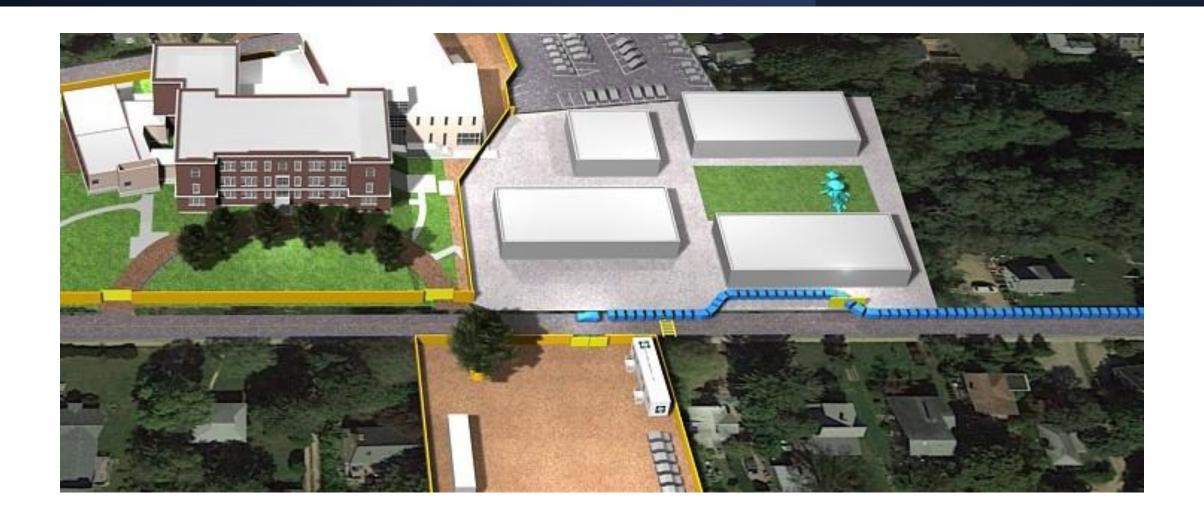

DESIGN & PROCUREMENT SCHEDULE

Milestone item	Lead Responsibility	Duration (Weeks)	Start	Finish	Remarks			
60% Construction Documents								
60% CD Pricing Set Issued	Тарре			28-Feb-22	Received - in progress			
60% CD Design Review & Cost Estimating	WTR/Tappe	3.5	28-Feb-22	24-Mar-22				
60% CD Reconciliation, Value Engineering	СНА	2	24-Mar-22	7-Apr-22	Reconciliation meeting 3/29			
Town Approval	Town	1	7-Apr-22	14-Apr-22				
100% Construction Documents and GMP Establishment								
Prepare, Issue and Review 100% Construction Docs for Bidding	Tappe			6-May-22	Tappe to provide 100% Bid Docs by 4/29 for review.			
Bid and Award Expedited Contracts	WTR	6	7-May-22	18-Jun-22	All Trade Contracts plus selective expedited non-trade (TBD)			
Establish and Execute GMP	Team	3	18-Jun-22	9-Jul-22				
Town Approval	Town	1	9-Jul-22	16-Jul-22				

CONSTRUCTION SCHEDULE — MOBILIZATION/EARLY WORK

Milestone item	Lead Responsibility	Duration (Weeks)	Start	Finish	Remarks	
Mobilization / Early Enabling						
Exploratory Demolition and Exploration	WTR	1	28-Feb-22	4-Mar-22		
Clear 55 West Williams Street, Mobilize Construction Trailers, Storage, Temp. Construction Fence, etc.	WTR	8	7-Mar-22	2-May-22		
Clear and Make Ready for Temp. Modulars	WTR/Tappe/Town of Tisbury	3	2-May-22	23-May-22	Includes School starting process of <b>MOVEOUT</b>	
Construct Temp Modulars	WTR/Tappe/Town of Tisbury	13.5	23-May-22	25-Aug-22	Occupancy Permit issued for start of School (Sept 2022)	

CONSTRUCTION SCHEDULE — EARLY/FULL CONSTRUCTION

Milestone item	Lead Responsibility	Duration (Weeks)	Start	Finish	Remarks		
Early & Full Construction							
Gym Separation from Existing Building	WTR	1	19-Apr-22	22-Apr-22			
Site Utilities Required for Demolition	WTR	10	19-Apr-22	28-Jun-22			
Abatement of Gymnasium	WTR	13	22-Apr-22	22-Jul-22			
Demolition of Existing Gymnasium	WTR	10	27-Jun-22	5-Sep-22			
Full Construction	WTR	77	5-Sep-22	26-Feb-24	Target Occupancy - 3/1/24		
Final Site Finishes	WTR	24	26-Feb-24	12-Aug-24			

# QUESTIONS

#### **STAY INFORMED | BUILDING COMMITTEE + TOWN RESOURCES**

**READ MORE HERE!** 

Tisbury School Project Website:

www.tisbury-school-project.com

**EMAIL US!** 

Tisbury School Building Committee:

tisburyschoolproject@gmail.com

Sign-up for Town e-Alerts!

Town of Tisbury Website:

www.tisburyma.gov
